

Slovak University of Technology in Bratislava

Faculty of Informatics and Information Technologies

NAO ROBOT EXERCISE SYSTEM

Sprint 0 Retrospective

15 October – 25 October 2026

Team Leaders

Ing. Jakub Perdek, PhD.
doc. Ing. Fedor Lehocki, PhD.

Team Members

Bc. Akhmadinurov Amal
Bc. Danilov Denis
Bc. Dmitriev Anton
Bc. Gainetdinov Ruslan
Bc. Kuzin Timofei
Bc. Tikhoblazhenko Alena
Bc. Zimnitski Aliaksei

Bratislava • 2026/2027

1 Meeting Details

At the end of Sprint 0, the NAOMI team met to evaluate the sprint in a Scrum retrospective. Sprint 0 was a preparatory sprint focused on organizing the team and understanding the project.

Table 1: Retrospective meeting

Item	Details
Date and time	Monday, 26 October 2026, 16:00
Place	NAO robot laboratory, FIIT STU
Retrospective for	Sprint 0 (15 October – 25 October 2026)
Participants	All team members: A. Akhmadinurov, D. Danilov, A. Dmitriev, R. Gainetdinov, T. Kuzin, A. Tikhoblazhenko, A. Zimnitski
Prepared by	Bc. Gainetdinov Ruslan

2 Sprint Outcome

The team completed 16 of 17 tasks of Sprint 0. One task was not completed: **SCRUM-28 Request and secure faculty server**. The faculty assigned the server to the team, but connecting to it and securing it took more time than expected, so the task was moved to Sprint 1.

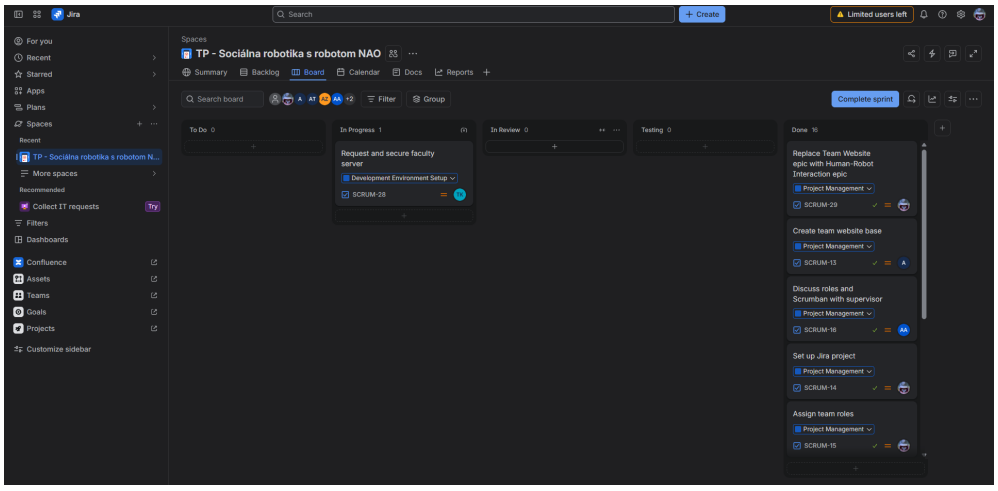


Figure 1: Board of Sprint 0 at sprint closure

The main results of the sprint were the team's working environment (Jira project, GitHub organization, fork of the existing repository, documentation repository with automatic publishing), the first team methodologies and the project description and goals.

3 Team Meetings in the Sprint

13 October 2026 (Microsoft Teams) – sprint planning. The team defined the first tasks: organizing the team and its tools, analyzing the existing project to understand what needs to be done, and preparing questions to clarify with the supervisor.

19 October 2026 (Microsoft Teams). The team went through the topics discussed with the supervisor on 16 October 2026, turned them into concrete tasks and assigned at least one task to each team member. Topics that were still unclear were recorded as questions for the next supervisor meeting.

4 Course of the Meeting

The meeting took place in the laboratory with the NAO robot. It started with a short summary of Sprint 0: the team went through the completed tasks and discussed the one task that was not completed (SCRUM-28) and the reason for the delay.

The team agreed that from Sprint 1 all work will follow the methodologies created in Sprint 0. In particular, every task planned into a sprint will be estimated in story points according to the backlog management methodology, so that the team velocity can be tracked in the following sprints.

In the second part of the meeting, the team tried to connect to the real NAO robot with the existing solution. The connection did not work out of the box: the services had missing dependencies, and the robot address and port could not be configured without editing the Docker Compose files. These problems were turned into Sprint 1 tasks (SCRUM-51, SCRUM-52 and SCRUM-57).

5 Changes for Sprint 1

Based on the retrospective, the team introduced the following changes from Sprint 1:

- Every task in a sprint has an epic, an assignee, a story point estimate and a

priority. Estimates follow the scale in the backlog management methodology.

- Changes to code and documents are merged only through pull requests with a description (Changes, Reason, Verification) and approvals from other team members.
- New tasks are created right after supervisor meetings, so that the backlog reflects the agreed scope.
